BOREWELL COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 846

Date : 30/9/19.

1. Customer's Name and Address with Telephone No. : AEE BBMP Byatarayanapura Sub Divn

2. Well Location : Pacchenahally Near over Tank

3. Total Well Depth / Drilled in Ft. : 1227 feet.

4. Casing Erected in Ft. : 214 feet.

5. Water Struck at the Depth of : 680 feet. 840 feet 1160 feet

6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear clear

8. At the Depth of : 1160 feet.

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

Party's Signature

For VINAYAKA ENTERPRISES

Manager / Proprietor

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : ALE BBMP

b) Location of the Site : Byatarayanapura Bug division

c) Area of the land : Raghavendra Nagar over Tank

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneiss Weathered Chlorite

2) Recommended Site for drilling : Ward No. 06

3) Total depth to be drilled : 1020' to 1265'

4) Approx. casing pipe required : 182' to 230'

5) No. of water bearing Zones : - 3 -

6) No. of favourable spots marked : - 8 -

7) Qty. of water expected : 2 inch

8) Method of survey carried out : Geophysical method

9) Remarks : 6/12" dia Borewell

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

P.T.O. : *Terms & Conditions*

BOREWELL SITE PLAN

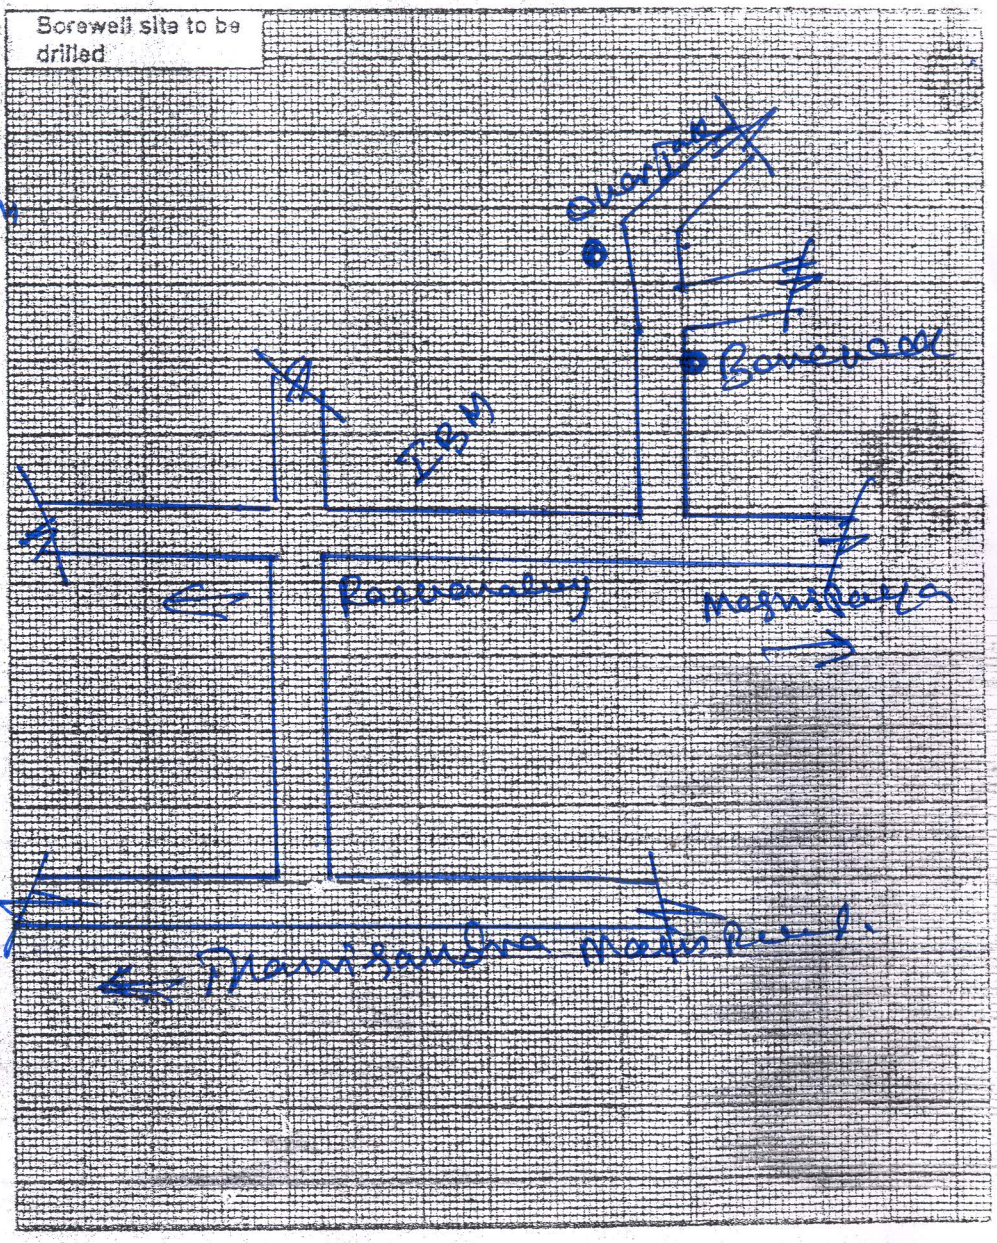

Party ... Well / (Authorised signatory) fully understood the terms ... depend upon the nature / formation of

BOREWELL
COMPLETION REPORT

VINAYAKA ENTERPRISES

Borewell Drilling Contractors

Mobile : +91 9342202932 / 9343202932

No. 9, Bhadrappa Layout, Bhadrappa Compound, Near Hebbal, Ring Road, Bangalore 560094

No. : 844

Date : 30/9/19

1. Customer's Name and Address : AEE BBMP
   with Telephone No. Byatarayanapura Sub Division

2. Well Location : Meggripalya (Scheme C)

3. Total Well Depth / Drilled in Ft. : 1233 feet.

4. Casing Erected in Ft. : 209 feet

5. Water Struck at the Depth of : 600 feet. 820 feet and 1100 feet

6. Total Yield (Measuring method "V" Norch : 2 inch / Inches on "V" Norch)

7. Formation of Soil/Well Water Condition : Boulders/Silt/Loose Soil/Clear Clear

8. At the Depth of : 1100 feet

9. Recommended to use Jet Pump / Air Compressor / Submersible /Hand Pump

The Borewell was drilled in accordance with the company terms and conditions and handed over to customer in good/ satisfied / Party agreed conditions.

Once the well handed over to party, company is no way responsible for further developments if anything in the well or what so ever.

Party's Signature

I, owner of the Well / (Authorised signatory) fully understood the terms and conditions and the well completion report, I also fully understood the quality and quantity of water from the well duly depend upon the nature / formation of ground water and the drilling agency no way responsible for further occurrence / Changes in the bore with full satisfaction. I hereby endorse my signature.

For VINAYAKA ENTERPRISES

Party's Signature

Manager / Proprietor

GROUND WATER SURVEY REPORT

OPEN WELL/ BOREWELL
DATA OF SURVEY

a) Name of the Party : AEE BBMP Byatarayanapura Sub Div

b) Location of the Site :

c) Area of the land : Meghripalya School

INVESTIGATION REPORT

1) GEOLOGY OF THE AREA : Gneissic Rock

2) Recommended Site for drilling : Ward No. 06

3) Total depth to be drilled : 1010' to 1870'

4) Approx. casing pipe required : 182 to 220'

5) No. of water bearing Zones : — 3 —

6) No. of favourable spots marked : — 8 —

7) Qty. of water expected : 2 inch

8) Method of survey carried out : Geophysical Method

9) Remarks : 6 [12' Dia Borewell

HYDROGEOLOGIST
(M.G. RAJASHEKHAR, M.Sc., DEG., F.G.S.)

T.O. : Terms & Conditions

BOREWELL SITE PLAN
